


Construction Timeline Comparison

Original Timeline




Actual Timeline

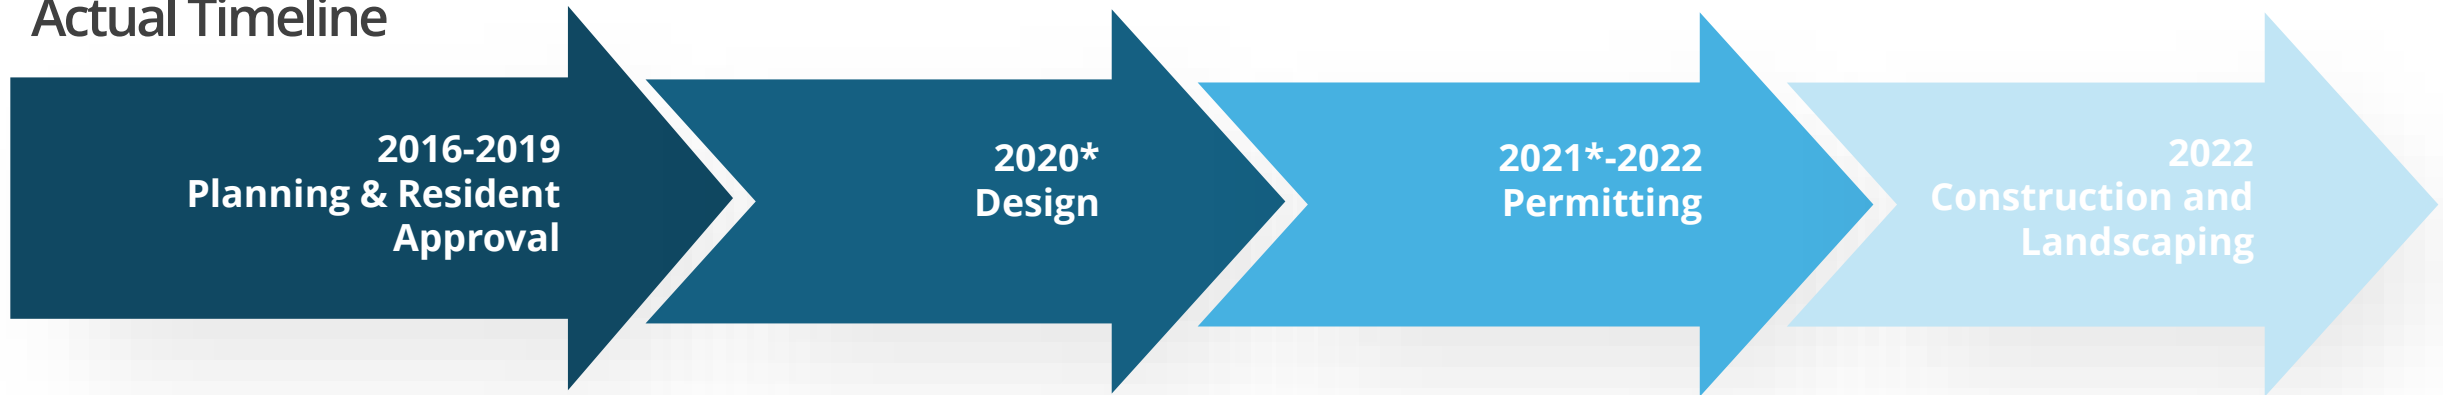

*COVID-19 Pandemic

Construction Timeline Comparison

Original Timeline

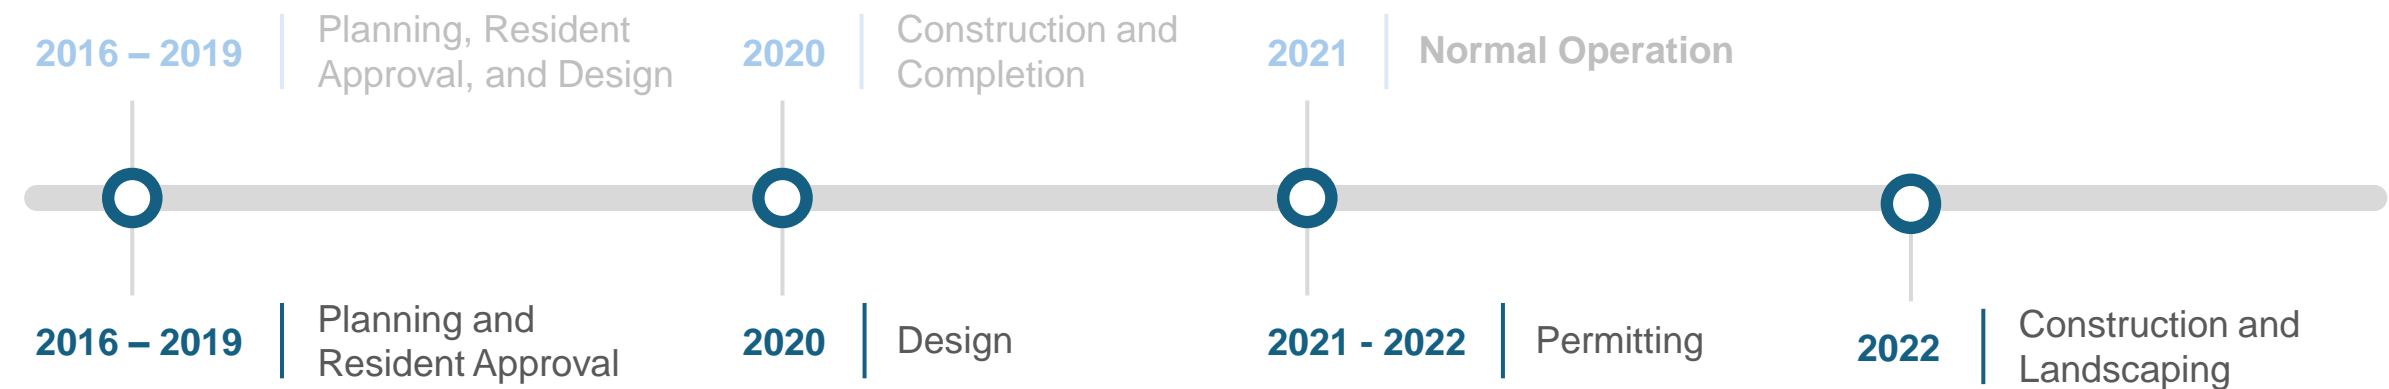

Actual Timeline

 *2020 COVID-19 Outbreak



Budget

During and after the COVID-19 pandemic, construction costs saw a **national average increase of 40%.**

However, **our team completed the project with only an 11.98% increase** from the originally approved budget.

Project Estimate at Onset: \$740,163

Actual Project Cost Upon Completion: \$834,452.82

*Fiscal Year is October 1 – September 30
